LOCATION MAP

Pt of SEC 24 & 25, T 18 N, R 16 E,
Pt of SEC 19 & 30, T 18 N, R 17 E,
CITY OF OSHKOSH
WINNEBAGO COUNTY, WI

Based on Winnebago County Coordinate System

Point Number	Northing	Easting	Monument Replaced
25002	470107.45	796881.37	Drill Hole
25003	470369.26	796503.73	3/4" Iron Rod
25004	470422.47	796427.13	Drill Hole
25005	470317.04	796484.30	3/4" Iron Rod
25006	470345.49	796443.50	3/4" Iron Rod
25008	470394.61	796379.03	3/4" Iron Rod
25009	470561.04	796221.40	Drill Hole
25010	470647.24	796139.40	3/4" Iron Rod
25011	470700.42	796089.12	Drill Hole
25012	470775.12	796092.66	3/4" Iron Rod
25013	470949.37	795927.64	3/4" Iron Rod
25014	471043.91	795838.36	Drill Hole
25015	469727.22	797458.48	Drill Hole
25016	469935.14	797128.38	Drill Hole
25017	469833.18	797476.70	Drill Hole
25018	469873.13	797483.72	Drill Hole
25019	469937.99	797545.29	3/4" Iron Rod
25020	469993.04	797554.64	Drill Hole
25021	470662.52	797620.61	Drill Hole
25022	470870.38	797656.75	Drill Hole
25023	471061.79	797689.84	Drill Hole
25024	471111.04	797698.34	Drill Hole
25026	470141.93	798036.56	Drill Hole
25028	470062.48	798011.69	3/4" Iron Rod
25029	469998.36	797984.90	3/4" Iron Rod
25030	470155.76	797978.33	Drill Hole
25031	470080.87	797954.64	3/4" Iron Rod
25032	469856.48	797858.75	Drill Hole
25033	469805.22	797836.94	Drill Hole
25034	469745.44	797811.47	Drill Hole
25035	469690.94	797787.80	3/4" Iron Rod
25036	469635.71	797764.50	Drill Hole
25037	470294.26	798021.85	Drill Hole
25038	470594.62	798141.63	MC (Set Masonry (MAG) Nail in Conrete)
25039	470557.87	798143.04	WC (Set 3/4" Iron Rod)
25040	470575.79	798094.23	WC (Set 3/4" Iron Rod)
25041	470649.72	798110.81	WC (Set 3/4" Iron Rod)
25042	470651.31	798164.04	WC (Set 3/4" Iron Rod)
25043	470717.73	798178.34	Drill Hole
25044	470677.32	798107.88	3/4" Iron Rod
25045	470586.08	798087.51	3/4" Iron Rod
25046	470982.28	798237.88	Drill Hole
25047	470337.75	798093.28	Drill Hole
25048	469896.86	797101.10	MC (Set 1 1/4" Iron Rod)
25049	469914.89	797064.85	WC (Set 3/4" Iron Rod)
25050	469951.06	797089.88	WC (Set 3/4" Iron Rod)
25051	469906.51	797157.49	WC (Top Nut of Existing Water Hydrant)
25052	469870.69	797127.68	WC (Set 3/4" Iron Rod)

NOTES

This Monumentation Survey is for the purpose of replacing monuments as located prior to road/utility construction (Project #1652). A list of monuments that were destroyed during construction was provided to Davel Engineering and Environmental Inc. by the City of Oshkosh Engineering Department. Monuments were replaced in accordance to said list. Note the replaced monuments may not match the same size or material of the found monuments.

Lot Lines are shown per City of Oshkosh mapping. Lot lines are shown for location representation only, lot lines may vary.

This is not a boundary survey.

SURVEYOR'S CERTIFICATE

I, James R Sehloff, hereby certify that under my control, the replaced monuments shown on this map were set on Decemeber 29, 2017 as found and located on April 20, 2017. I **do** certify the accuracy of the replaced monuments to represent the location of the monument as located on said date, but I **do not** certify the accuracy of the replaced monuments in relation to the true property corner. I hereby certify that said Monumentation Survey and map were made in accordance with acceptable professional standards and that the information contained thereon is, to the best of my knowledge, information and belief, a true and accurate representation thereof.

JAMES R SEHLOFF S-2692 DE PERE LAND SURVEYOR

31 JAN 2018

James R Sehloff, Wisconsin Professional Land Surveyor No. S-2692 Date

80 0 80 160 240

Coordinates are referenced to the Winnebago County Coordinate System.



LEGEND

- Replaced Monument (See Chart for Description)
- Witness Monument (WC)
- Government Corner (MC)
- 1215 Property Address (per provided City mapping)

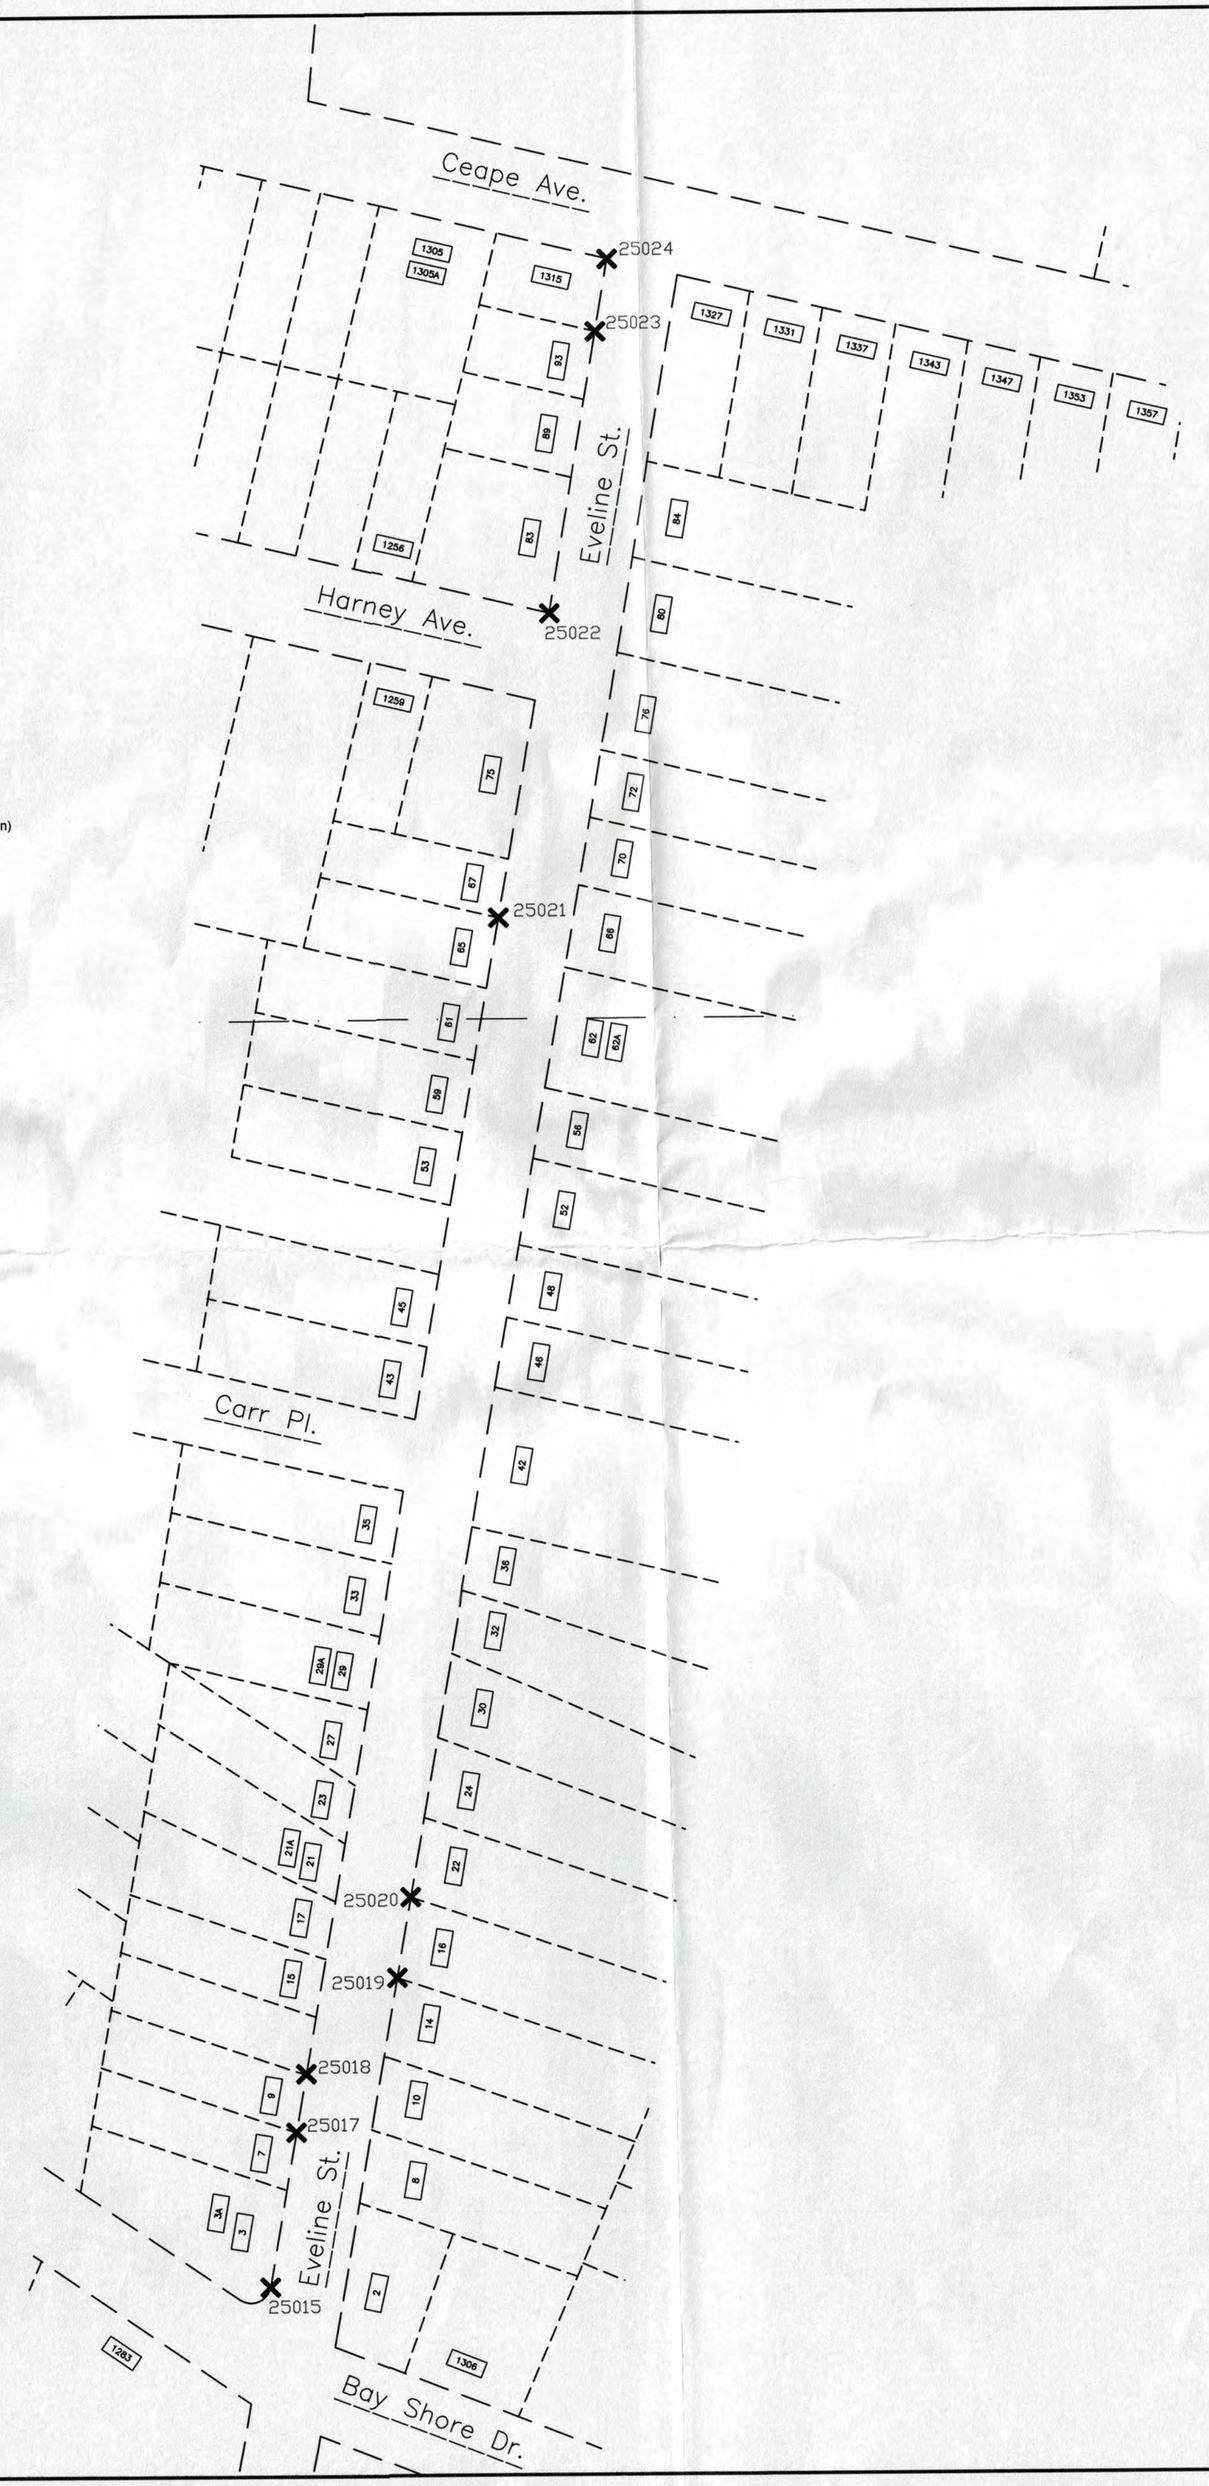

Jan 05, 2018 - 12:38 PM J:\Projects\4949corr\dwg\Corrison\4949 monuments (Reset Mon).dwg

DAVEL ENGINEERING & ENVIRONMENTAL, INC.
CIVIL ENGINEERING CONSULTANTS
1811 Racine Street Menasha, WI 54952
Ph: 920-991-1866 Fax: 920-830-9595
www.davel.pro

MONUMENTATION SURVEY

Contract 17-04 Property Monuments (Bid Project #1652)

City of Oshkosh, Winnebago County, WI
For: City of Oshkosh

Date: 01/5/2018
Filename: 4949 monuments (Reset Mon).dwg
Author: SRA
Last Saved by: scott
Page 2 of 2
